

Dr. Bob Harrington
Inyo County Water Department
135 South Jackson Street
Independence, CA 93526

April 30, 2012

RE: Summary of Hydrologic Monitoring Activities April 2012
Rose Valley, Inyo County, California
Hay Ranch Project Conditional Use Permit #2007-03

Dear Dr. Harrington:

This letter is intended to summarize hydrologic monitoring activities conducted in April 2012 by TEAM Engineering & Management, Inc. (TEAM), related to the Hay Ranch Water Extraction Project and CUP #2007-03.

Background

As outlined in the Hay Ranch Water Extraction Final EIR's Hydrologic Monitoring and Mitigation Plan (HMMP), Phase 1: Monitoring System Setup and Supplemental Data Collection occurred prior to December 25, 2009 at monitoring points throughout Rose Valley. With the initiation of pumping by Coso Operating Company (Coso) on December 25, 2009, the Hay Ranch Water Extraction Project entered into the Phase 2: Startup Monitoring and Reporting period. Phase 3: Model Recalibration and Redefinition of Pumping Rates and Durations occurred from September 2010 to April 2011, with recalibration of the groundwater model by Daniel B. Stephens & Associates (DBS&A) and with redefinition of pumping rates and durations by Inyo County Water Department (ICWD). With the April 1, 2011 issuance of the ICWD's "Addendum to the HMMP for CUP#2007-003/Coso Operating Company, LLC" (2011 ICWD Addendum) the project has entered Phase 4: Ongoing Monitoring, Mitigation and Reporting.

Monitoring and Reporting

During the April 2012 monthly hydrologic data collection event at 30 monitoring locations in the Rose Valley area, static depth-to-water (DTW) measurements, one visual observation of the Little Lake Ranch (LLR) Siphon Well Outflow and four sets of flow rates were collected by TEAM, as summarized in the attached table (Table 1). Data for this monthly field event was collected on April 18 and 19. Pressure transducer data were downloaded from 24 units, including one "BaroTroll" measuring barometric pressure. On April 3, a DTW measurement at LADWP 816 Well was taken by LADWP personnel.

At the Hay Ranch Property, Coso has pumped groundwater from two production wells: Hay Ranch North and Hay Ranch South. For the first year of project pumping, December 25, 2009 to December 31, 2010, a total of approximately 2992 acre feet (AF) of groundwater were extracted from these two wells (821 AF from the Hay Ranch North Well, and 2171 AF from the Hay Ranch South Well).

For the second year of project pumping, January 1, 2011 to January 1, 2012, a total of approximately 3895 AF of groundwater were extracted from the Hay Ranch property (1289 AF from the Hay Ranch North Well, and 2606 AF from the Hay Ranch South Well).

For the third year of project pumping, from January 1, 2012 to April 18, 2012, a total of approximately 996 AF of groundwater have been extracted from the Hay Ranch property (4 AF from the Hay Ranch North Well, and 992 AF from the Hay Ranch South Well).

Figure 1 presents the combined amount of groundwater pumped from the Hay Ranch North and South wells (in AF) from December 25, 2009 through April 18, 2012 compared to a hypothetical pumping amount. The total amount of groundwater extracted from the Hay Ranch property from December 25, 2009 to April 18, 2012 (Hay Ranch CUP project total) is approximately 7883 AF. The hypothetical pumping amount assumes a pumping rate of approximately 3000 acre-feet per year (AFY) for December 25, 2009 through December 31, 2010 and assumes a pumping rate of approximately 4839 AFY from January 1, 2011 through December 31, 2012. These hypothetical pumping rates represent the maximum allowable pumping amounts for the 2010, 2011 and 2012 periods.

Trigger Levels and Maximum Acceptable Drawdowns

In Table 2 of the 2011 ICWD Addendum, drawdown at cessation of pumping trigger levels (Trigger Levels) have been set for specific monitoring wells based on an annual pumping rate of 4839 AFY.

Based on the manual DTW data collected by TEAM on April 18-19, 2012, no Trigger Levels or Maximum Acceptable Drawdowns have been exceeded at Hay Ranch Project monitoring wells which have baselines and trigger levels established.

Quarterly Groundwater Monitoring

On March 15, 2012, groundwater samples were collected from the Hay Ranch South, Coso Junction Store #2, and Little Lake Ranch North as part of the quarterly monitoring activities specified in the HMMP. These groundwater samples were analyzed for total dissolved solids (TDS) by TestAmerica, Inc. a California-Certified Analytical Laboratory. None of the three samples exceeded Threshold Requiring Action Levels.

Operational Notes

The pressure transducer installed at Little Lake Ranch North Well displayed signs of power failure and will be replaced. Data was recovered from the unit and is included in the April hydrographs.

Data Transmittal

TEAM posted updates to the “Coso” database on the ICWD web server. New Hay Ranch Project hydrographs in PDF form were uploaded to the ICWD website (www.inyowater.org).

* * * * *

If you have any questions or require additional information, please contact TEAM at your convenience.

Sincerely,

TEAM Engineering & Management, Inc.

Keith Rainville
Staff Geologist

TABLE 1
Field Observations of Rose Valley Hydrologic Monitoring Points
April 18-19, 2012

Project Name:	Hay Ranch Project HMMP	Date: April 18-19, 2012
Location:	Rose Valley, Inyo County	
Observer(s):	K. Rainville	Page: 1 of 1

Well ID	Monitoring Point	Date	Time	DTW (ft)	Flow (cfs)	GWE (ft amsl)	Method	Transducer Log Interval	Notes
RV-10	Dews	04/18/12	14:00	231.37		3755.55	TEAM manual read	NA	
RV-20	LADWP 816	04/03/12	12:52	77.33		3437.73	LADWP manual read	NA	Data provided by LADWP
RV-30	Cal Pumice	04/18/12	9:42	256.18		3249.71	TEAM manual read	Hourly	
RV-40	Dunmovin	04/19/12	9:00	303.11		3244.76	TEAM manual read	NA	
RV-50	Hay Ranch North	04/18/12	10:44	NM	No	NM	TEAM manual read	NA	668,855,329 gallons (2114 AF) pumped since 12/25/09
RV-60	Hay Ranch 1A	04/18/12	10:30	203.62		3228.55	TEAM manual read	Hourly	
RV-61	Hay Ranch 1B	04/18/12	10:35	227.80		3204.05	TEAM manual read	Hourly	
RV-62	Hay Ranch 1C	04/18/12	10:40	216.57		3214.93	TEAM manual read	Hourly	
RV-70	Hay Ranch South	04/18/12	10:45	NM	Yes	NM	TEAM manual read	NA	1,879,900,807 gallons (5769 AF) pumped since 12/25/09
RV-80	Hay Ranch 2A	04/18/12	10:55	202.53		3230.47	TEAM manual read	Hourly	
RV-81	Hay Ranch 2B	04/18/12	11:01	233.64		3198.99	TEAM manual read	Hourly	
RV-82	Hay Ranch 2C	04/18/12	11:07	216.03		3216.07	TEAM manual read	Hourly	
RV-90	Coso Jct Ranch	04/18/12	10:00	173.07		3230.06	TEAM manual read	Hourly	
RV-100	Coso Jct Store #1	04/18/12	10:14	146.40		3225.72	TEAM manual read	Hourly	
RV-110	Davis Ranch North Well	04/18/12	13:01	6.47		3886.53	TEAM manual read	Hourly	
RV-111	Davis Ranch South Well	04/18/12	13:14	11.30		3886.76	TEAM manual read	Hourly	
RV-112	Davis Ranch South Flow	04/18/12	13:27	NA	0.12	NA	TEAM manual read	Hourly	
RV-120	Red Hill Well (BLM)	04/18/12	11:32	139.80		3201.03	TEAM manual read	Hourly	
RV-130	G-36	04/18/12	11:50	180.38		3199.64	TEAM manual read	NA	
RV-140	Lego	04/19/12	12:49	222.40		3200.45	TEAM manual read	Hourly	
RV-150	Cinder Road	04/18/12	12:30	191.00		3186.96	TEAM manual read	Hourly	
RV-160	18-28 GTH	04/19/12	12:33	173.84		3188.74	TEAM manual read	Hourly	
RV-170	Fossil Falls Campground	04/18/12	12:18	141.19		3175.58	TEAM manual read	NA	
RV-180	LLR North Well	04/19/12	10:15	40.18		3158.92	TEAM manual read	Hourly	
RV-210	LLR Dock Well	04/19/12	10:46	6.12		3148.02	TEAM manual read	Hourly	
RV-220	LLR Stilling Well (lake surface)	04/19/12	10:51	3.54		3147.50	TEAM manual read	Hourly	
RV-230	LLR Little Lake Outflow	04/19/12	11:20	NA	0.03	NA	TEAM manual read	Hourly	
RV-240	LLR Coso Springs Flow	04/19/12	11:07	NA	0.39	NA	TEAM manual read	Hourly	
RV-245	LLR North Culvert Flow	04/19/12	11:45	NA	0.81	NA	TEAM manual read	Hourly	
RV-250	LLR Siphon Discharge	04/19/12	11:40	NA	Yes	NA	TEAM visual read	NA	Siphon Well flowing into Pond 2
RV-260	LLR Hotel Well	04/19/12	9:32	0.32		3138.46	TEAM manual read	Hourly	

NM - not measured; NA - not applicable; IO - Inoperative

DTW - Depth to water in feet (ft) below top of casing or other reference point; a negative DTW indicates that the groundwater elevation is above the surveyed reference point

Flow - In cubic feet per second (cfs)

GWE- Groundwater elevation in feet above mean sea level (ft amsl)

TABLE 2
Hay Ranch Project Groundwater Baselines and Trigger Levels
April 2012


Well ID	Monitoring Point	Baseline GWE ¹ (feet amsl)	Recent Date of Measurement	Recent GWE (feet amsl)	Recent GWE Compared to Baseline (feet)	Recent GWE Above Max DD ² (feet)	Trigger Level At Cessation of Pumping ³ (feet)	Recent GWE Compared to Trigger Level (feet)
RV-40	Dunmovin	3252.73	04/19/12	3244.76	-7.97	15.33	23.2	15.23
RV-80	HR 2A	3240.92	04/18/12	3230.47	-10.45	17.15	27.6	17.15
RV-90	Coso Jct Ranch	3230.65	04/18/12	3230.06	-0.59	11.11	11.3	10.71
RV-100	Coso Jct Store #1	3227.59	04/18/12	3225.72	-1.87	8.23	9.5	7.63
RV-120	Red Hill Well	3200.66	04/18/12	3201.03	0.37	4.27	1.8	2.17
RV-130	G-36	3198.35	04/18/12	3199.64	1.29	4.69	1.0	2.29
RV-140	Lego	3199.21	04/19/12	3200.45	1.24	3.54	0.0	1.24
RV-150	Cinder Road	3186.92	04/18/12	3186.96	0.04	2.34	0.2	0.24
RV-160	18-28 GTH	3187.67	04/19/12	3188.74	1.07	3.17	0.0	1.07
RV-180	LLR North Well	3158.88	04/19/12	3158.92	0.04	1.34	0.0	0.04

1) GWE: Groundwater elevation measured in feet above mean sea level. Baseline GWEs set January 2010 and March 2011 and approved by Inyo County Water Department

2) Max DD: Maximum Acceptable Drawdown from Table 2 of "Addendum to HMMP for CUP#2007-003/Coso Operating Company, LLC"

3) Trigger Level at Cessation of Pumping from Table 2 of "Addendum to HMMP for CUP#2007-003/Coso Operating Company, LLC"

FIGURE 1
HYPOTHETICAL AND ACTUAL HAY RANCH PROJECT PUMPING

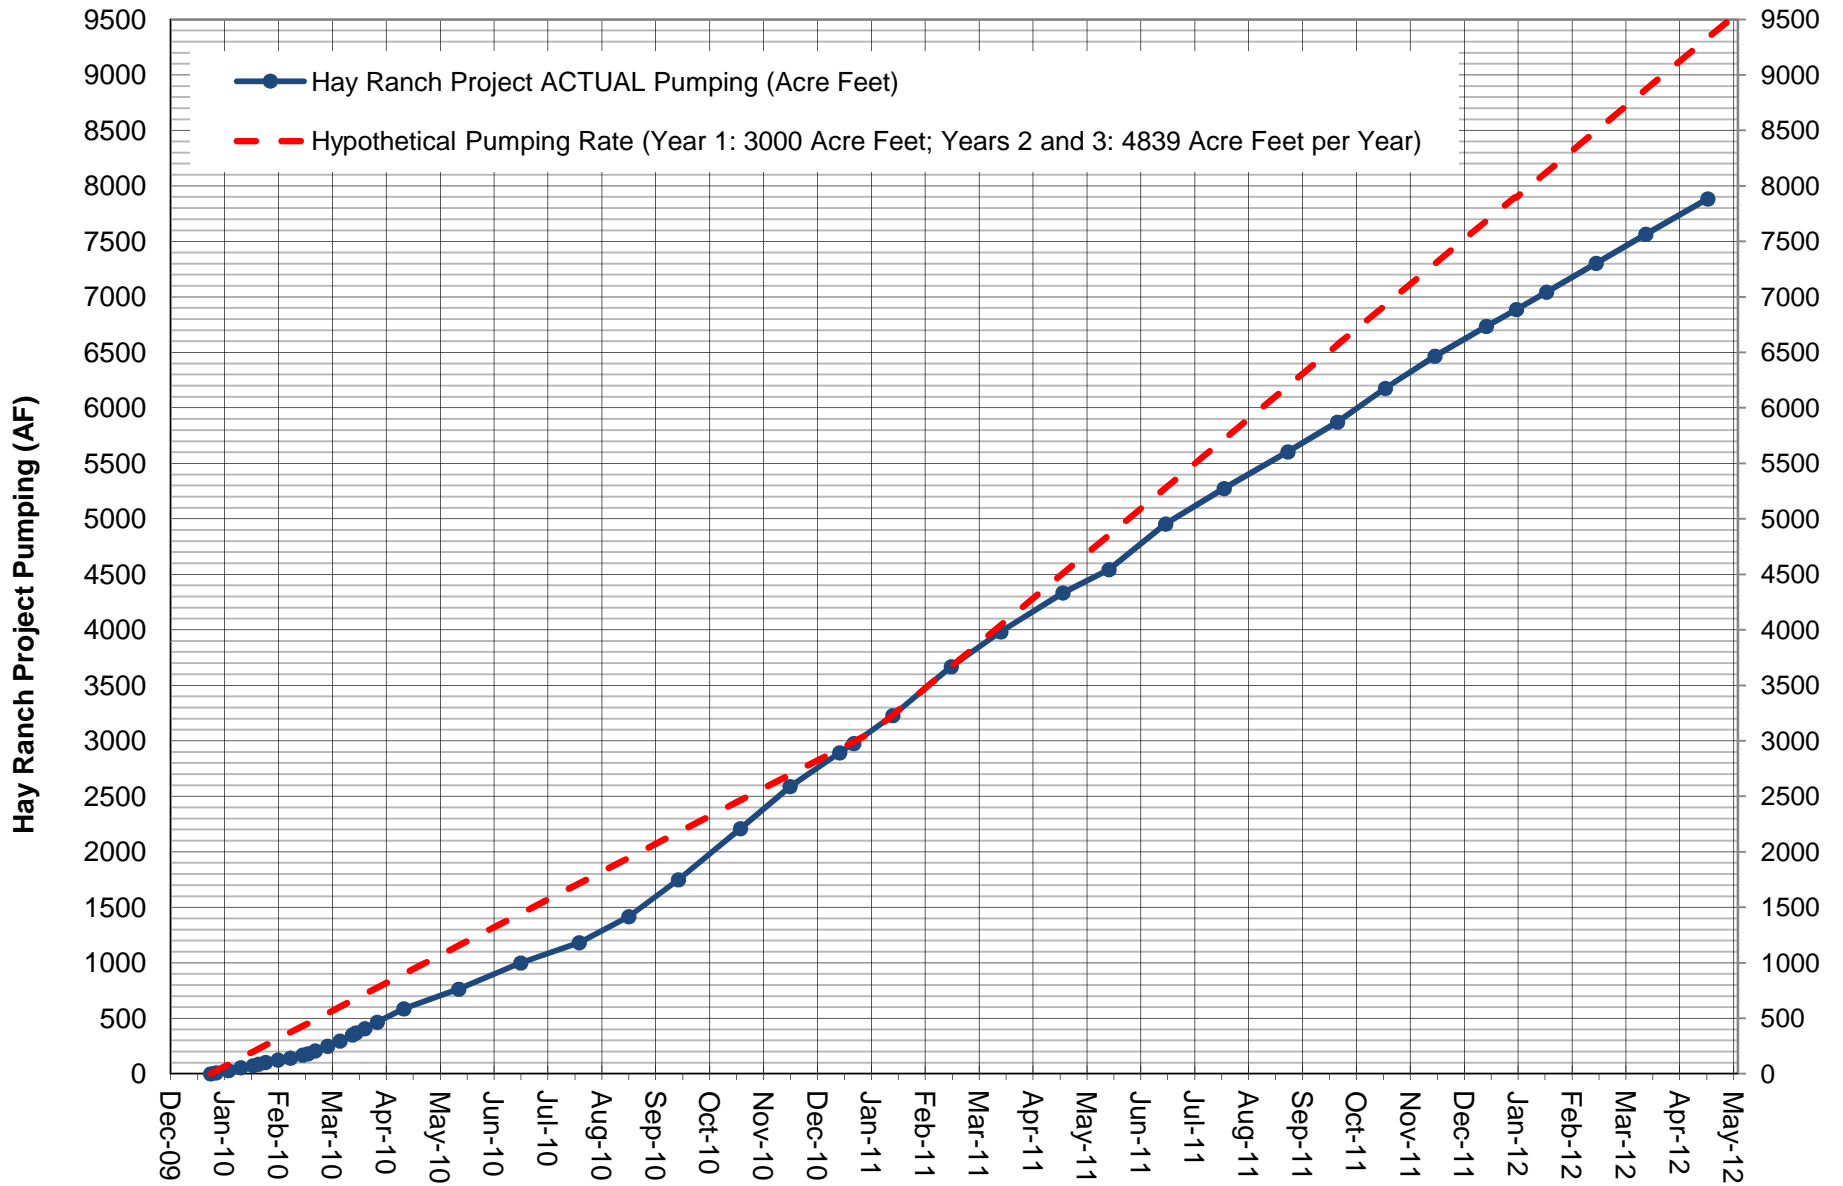

Note: Coso Operating Co. initiated Hay Ranch Project pumping on 12/25/09.

The "hypothetical pumping rate" is based on a pumping rate of 3000 AF per year for 12/25/09 to 12/31/10, and 4839 AF per year for 2011 and 2012.
