

Dr. Bob Harrington
Inyo County Water Department
135 South Jackson Street
Independence, CA 93526

August 1, 2014

RE: Summary of Hydrologic Monitoring Activities July 2014
Rose Valley, Inyo County, California
Hay Ranch Project Conditional Use Permit #2007-03

Dear Dr. Harrington:

This letter summarizes hydrologic monitoring activities conducted in July 2014 by TEAM Engineering & Management, Inc. (TEAM), related to the Hay Ranch Water Extraction Project and CUP #2007-03.

Background

As outlined in the Hay Ranch Water Extraction Final EIR's Hydrologic Monitoring and Mitigation Plan (HMMP), Phase 1: Monitoring System Setup and Supplemental Data Collection occurred prior to December 25, 2009 at monitoring points throughout Rose Valley. With the initiation of pumping by Coso Operating Company (COC) on December 25, 2009, the Hay Ranch Water Extraction Project entered into the Phase 2: Startup Monitoring and Reporting period. Phase 3: Model Recalibration and Redefinition of Pumping Rates and Durations occurred from September 2010 to April 2011, with recalibration of the groundwater model by Daniel B. Stephens & Associates (DBS&A) and with redefinition of pumping rates and durations by Inyo County Water Department (ICWD). With the April 1, 2011 issuance of the ICWD's "Addendum to the HMMP for CUP#2007-003/Coso Operating Company, LLC" (2011 ICWD Addendum) the project entered Phase 4: Ongoing Monitoring, Mitigation and Reporting. In August 2013 further model revision occurred with results and new trigger levels detailed in ICWD's August 30, 2013 letter to Chris Ellis, Site Manager, Coso Operating Company, LLC regarding Conditional Use Permit #2007-003/Coso. In June 2014 further model revision was conducted by DBS&A with results and new trigger levels detailed in ICWD's June 27, 2014 letter to Chris Ellis, Site Manager, Coso Operating Company, LLC regarding Conditional Use Permit #2007-003/Coso.

Monitoring and Reporting

During the July 2014 monthly hydrologic data collection event at 29 monitoring locations in the Rose Valley area, static depth-to-water (DTW) measurements, one visual observation of the Little Lake Ranch (LLR) Siphon Well Outflow and four sets of flow rates were collected by TEAM, as summarized in the attached table (Table 1). Data for this monthly field event was collected on July 23-24, 2014. Pressure transducer data was downloaded from 24 units, including one "BaroTroll" measuring barometric pressure. Also in July, a DTW measurement at LADWP 816 Well was taken by LADWP personnel.

At the Hay Ranch Property, COC has pumped groundwater from two production wells: Hay Ranch North and Hay Ranch South. For the current year of project pumping, January 2, 2014 to July 23, 2014, a total of approximately 889 AF of groundwater have been extracted from the Hay Ranch property (888 AF from the Hay Ranch North Well, and 1 AF from the Hay Ranch South Well).

Figure 1 presents the combined amount of groundwater pumped from the Hay Ranch North and South wells, in acre feet, from December 25, 2009 through July 23, 2014 compared to the maximum allowable pumping amount. The total amount of groundwater extracted from the Hay Ranch property from December 25, 2009 to July 23, 2014 (Hay Ranch CUP project total) is approximately 13,558 AF. The

maximum pumping rate was approximately 3,000 acre-feet per year (AFY) for December 25, 2009 through December 31, 2010; was 4,839 AFY from January 1, 2011 through August 30, 2013; was 3,040 AFY from September 2013 through June, 2014; and is 1,614 AFY from July 1, 2014 to date. Coso Operating Company has been and currently is pumping less than the maximum allowable amount of groundwater from the Hay Ranch Wells.

Trigger Levels and Maximum Acceptable Drawdowns

In Table 1 of the June 27, 2014 ICWD Letter to Coso Operating Company, drawdown at cessation of pumping trigger levels (Trigger Levels) have been set for specific monitoring wells based on a pumping rate of 1,614 AFY starting on July 1, 2014.

Based on manual DTW data collected by TEAM during the July 2014 monitoring event, no Trigger Levels or Maximum Acceptable Drawdowns have been exceeded at Hay Ranch Project monitoring wells which have baselines and trigger levels established.

Operational Notes

During the June to July 2014 period, the pressure transducer in Red Hill well (RV120) continued to experience power issues despite having a new battery back-up installed to correct this problem. This pressure transducer will be replaced with a new unit during the August field event. Also, seasonal root growth was pulled from the Davis Ranch South outflow flume (RV112).

Data Transmittal

TEAM posted updates to the “Coso” database on the ICWD web server. New Hay Ranch Project hydrographs in PDF form were uploaded to the ICWD website (www.inyowater.org).

* * * * *

If you have any questions or require additional information, please contact TEAM at your convenience.

Sincerely,

TEAM Engineering & Management, Inc.

Keith Rainville
Staff Geologist

TABLE 1
Field Observations of Rose Valley Hydrologic Monitoring Points
July 23-24, 2014

Project Name:	Hay Ranch Project HMMP	Date: July 23-24, 2014
Location:	Rose Valley, Inyo County	
Observer(s):	K. Rainville	Page: 1 of 1

Well ID	Monitoring Point	Date	Time	DTW (ft)	Flow (cfs)	GWE (ft amsl)	Method	Transducer Log Interval	Notes
RV-10	Dews	07/23/14	12:25	231.77		3755.15	TEAM manual read	NA	
RV-20	LADWP 816	06/04/14	5:15	83.30		3431.76	LADWP manual read	NA	Data provided by LADWP
RV-30	Cal Pumice	07/23/14	10:10	260.65		3245.24	TEAM manual read	Hourly	
RV-40	Dunmovin	NM	NM	NM		NM	TEAM manual read	NA	Discontinued due to new in-well infrastructure
RV-50	Hay Ranch North	07/23/14	14:50	NM	Yes	NM	TEAM manual read	NA	2,482,010,967 gallons (7617 AF) pumped since 12/25/09
RV-60	Hay Ranch 1A	07/23/14	15:00	200.37		3231.80	TEAM manual read	Hourly	
RV-61	Hay Ranch 1B	07/23/14	15:05	222.75		3209.10	TEAM manual read	Hourly	
RV-62	Hay Ranch 1C	07/23/14	15:10	219.25		3212.25	TEAM manual read	Hourly	
RV-70	Hay Ranch South	07/23/14	14:51	NM	No	NM	TEAM manual read	NA	1,935,974,114 gallons (5941 AF) pumped since 12/25/09
RV-80	Hay Ranch 2A	07/23/14	15:30	201.25		3231.75	TEAM manual read	Hourly	
RV-81	Hay Ranch 2B	07/23/14	15:25	222.00		3210.63	TEAM manual read	Hourly	
RV-82	Hay Ranch 2C	07/23/14	15:20	212.55		3219.55	TEAM manual read	Hourly	
RV-90	Coso Jct Ranch	07/23/14	10:40	174.65		3228.48	TEAM manual read	Hourly	
RV-100	Coso Jct Store #1	07/23/14	11:00	147.27		3224.85	TEAM manual read	Hourly	
RV-110	Davis Ranch North Well	07/23/14	11:20	6.56		3886.50	TEAM manual read	Hourly	
RV-111	Davis Ranch South Well	07/23/14	11:30	11.31		3886.75	TEAM manual read	Hourly	
RV-112	Davis Ranch South Flow	07/23/14	11:40	NA	0.008	NA	TEAM manual read	Hourly	
RV-120	Red Hill Well (BLM)	07/23/14	12:15	140.31		3200.52	TEAM manual read	Hourly	
RV-130	G-36	07/23/14	13:35	181.57		3198.45	TEAM manual read	NA	
RV-140	Lego	07/23/14	13:25	223.47		3199.38	TEAM manual read	Hourly	
RV-150	Cinder Road	07/23/14	12:45	191.47		3186.49	TEAM manual read	Hourly	
RV-160	18-28 GTH	07/23/14	13:05	174.24		3188.34	TEAM manual read	Hourly	
RV-170	Fossil Falls Campground	07/23/14	13:50	141.47		3175.30	TEAM manual read	NA	
RV-180	LLR North Well	07/24/14	10:15	40.56		3158.54	TEAM manual read	Hourly	
RV-210	LLR Dock Well	07/24/14	10:30	6.77		3147.37	TEAM manual read	Hourly	
RV-220	LLR Stilling Well (lake surface)	07/24/14	10:40	4.29		3146.75	TEAM manual read	Hourly	
RV-230	LLR Little Lake Outflow	07/24/14	11:25	NA	0.00	NA	TEAM manual read	Hourly	
RV-240	LLR Coso Springs Flow	07/24/14	11:10	NA	0.36	NA	TEAM manual read	Hourly	
RV-245	LLR North Culvert Flow	07/24/14	11:35	NA	2.63	NA	TEAM manual read	Hourly	
RV-250	LLR Siphon Discharge	07/24/14	11:25	NA	Yes	NA	TEAM visual read	NA	Siphon Well flowing into Pond 2
RV-260	LLR Hotel Well	07/24/14	9:40	0.85		3137.93	TEAM manual read	Hourly	

NM - not measured; NA - not applicable; IO - Inoperative; UA - Data currently unavailable

DTW - Depth to water in feet (ft) below top of casing or other reference point; a negative DTW indicates that the groundwater elevation is above the surveyed reference point

Flow - In cubic feet per second (cfs)

GWE- Groundwater elevation in feet above mean sea level (ft amsl)

TABLE 2
Hay Ranch Project Groundwater Baselines and Trigger Levels
July, 2014


Well ID	Monitoring Point	Baseline GWE ¹ (feet amsl)	Recent Date of Measurement	Recent GWE (feet amsl)	Recent GWE Compared to Baseline (feet)	Trigger Level At Cessation of Pumping ³ (feet)	Recent GWE Compared to Trigger Level (feet)	Recent GWE Above Max DD ² (feet)
RV-80	HR 2A	3240.92	07/23/14	3231.75	-9.17	15.3	6.13	7.33
RV-90	Coso Jct Ranch	3230.65	07/23/14	3228.48	-2.17	9.3	7.13	7.13
RV-100	Coso Jct Store #1	3227.59	07/23/14	3224.85	-2.74	8.3	5.56	5.66
RV-120	Red Hill Well	3200.66	07/23/14	3200.52	-0.14	3.0	2.86	3.66
RV-130	G-36	3198.35	07/23/14	3198.45	0.10	2.2	2.30	3.40
RV-140	Lego	3199.21	07/23/14	3199.38	0.17	0.7	0.87	2.57
RV-150	Cinder Road	3186.92	07/23/14	3186.49	-0.43	1.0	0.57	1.87
RV-160	18-28 GTH	3187.67	07/23/14	3188.34	0.67	0.7	1.37	2.77
RV-180	LLR North Well	3158.88	07/24/14	3158.54	-0.34	0.4	0.06	0.96

1) GWE: Groundwater elevation measured in feet above mean sea level. Baseline GWEs set January 2010 and March 2011 and approved by Inyo County Water Department (ICWD)

2) Max DD: Maximum Acceptable Drawdown from Table 1 of ICWD's "June 27, 2014 Conditional Use Permit#2007-003/Coso "

3) Trigger Level at Cessation of Pumping from Table 1 of ICWD's "June 27, 2014 Conditional Use Permit#2007-003/Coso "

FIGURE 1
ACTUAL AND MAXIMUM ALLOWABLE PUMPING FOR HAY RANCH PROJECT

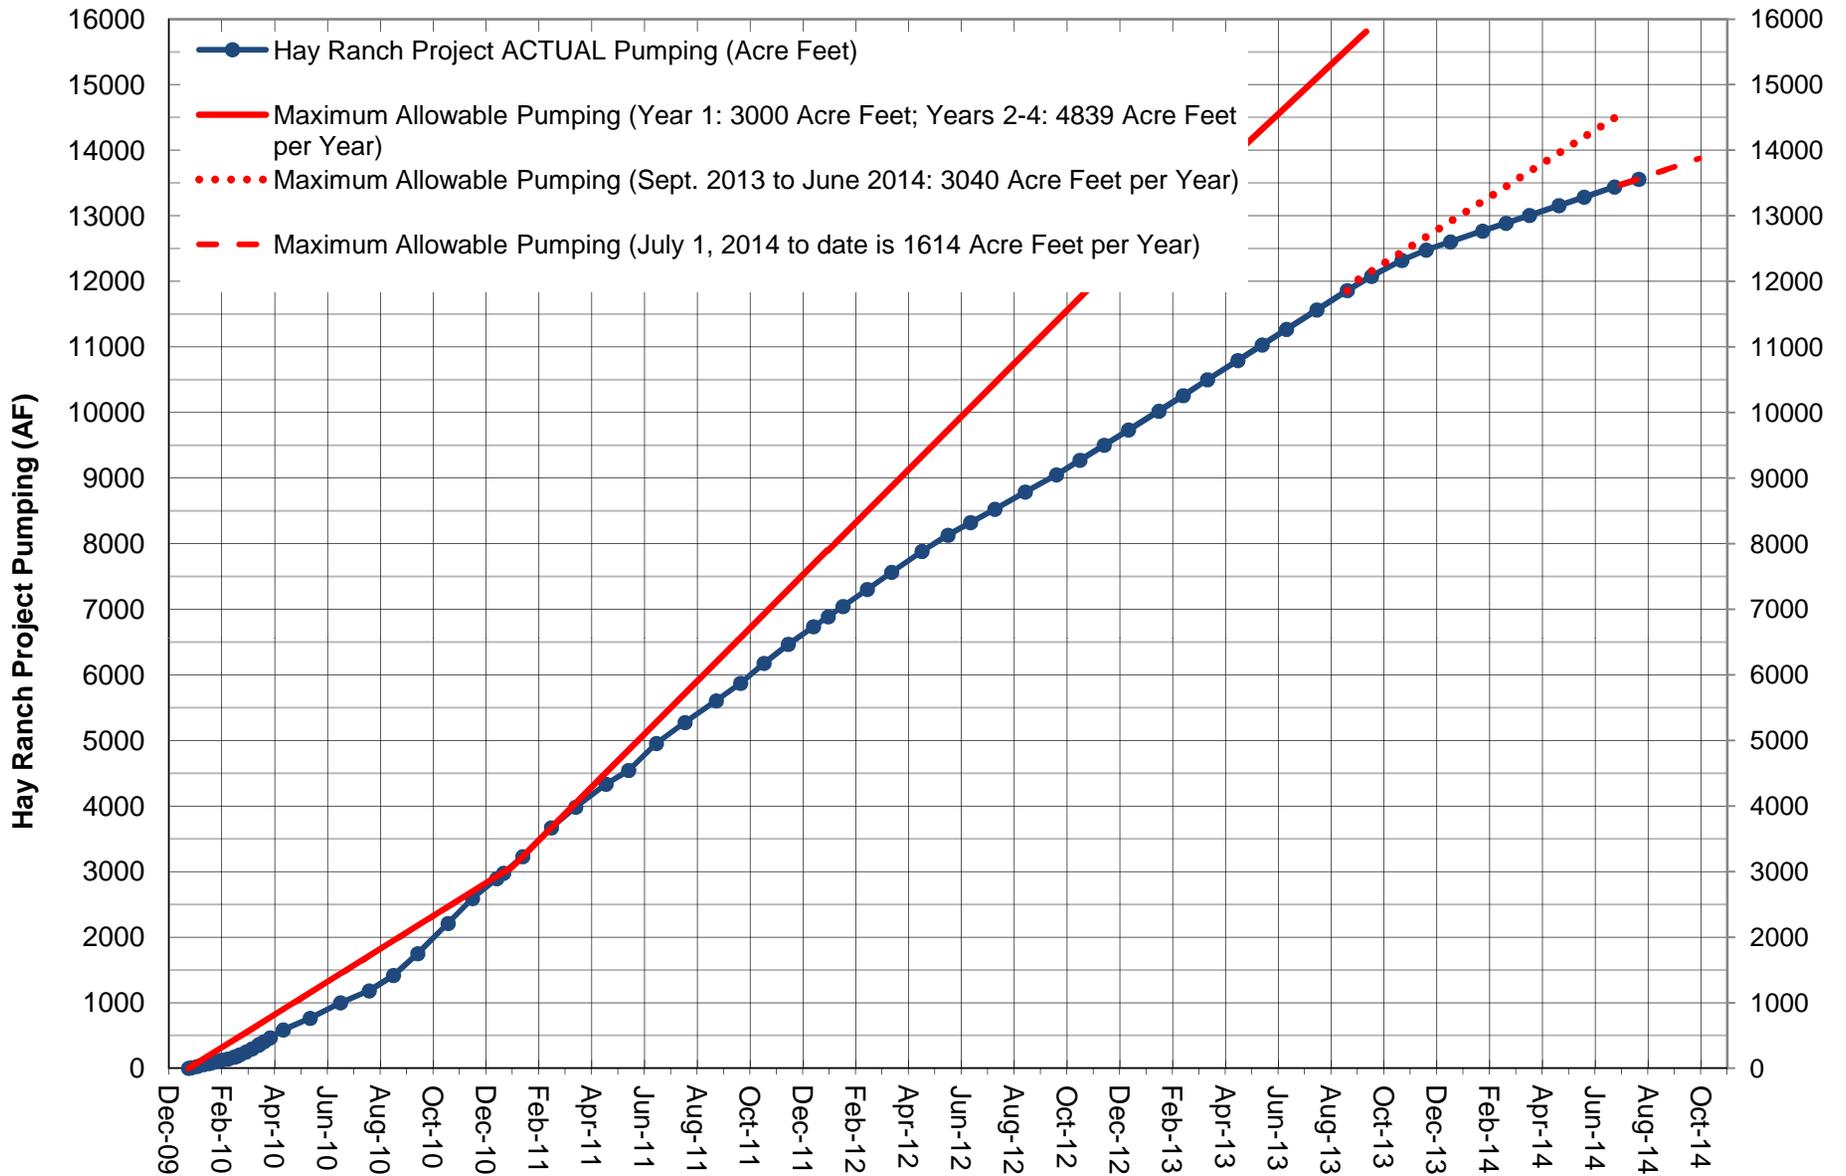

Note: Coso Operating Co. initiated Hay Ranch Project pumping on 12/25/09.

The "hypothetical pumping rate" is based on a pumping rate of 3000 AF/yr for 12/09 to 12/10, 4839 AF/yr for 1/11-8/13, and 3040 AF/yr from 9/13 to date.
